Transit-Oriented Development

TOD Project Updates

TriMet Board Briefing 01/24/24








Hollywood Transit Center – Infrastructure Project

- WHAT New infrastructure to update the 38-year-old transit center and support the planned 224-unit hollywoodHUB affordable housing development
- WHEN Phase 1 construction is underway. Phase 1 scheduled completion is Summer 2024
- WHAT Temporary ramp installed and operational.
 Demolition of the original stair/ramp structure nearing completion. Work starting on the new stair/ramp






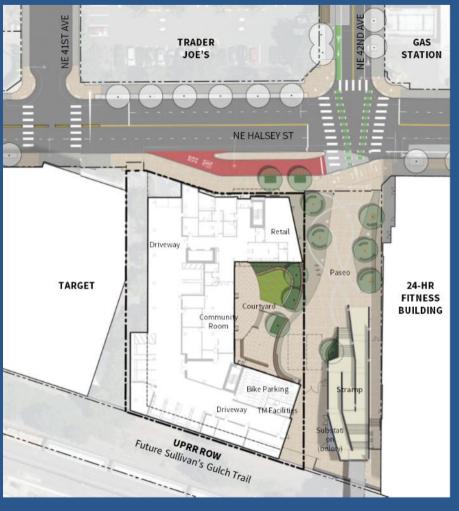


Hollywood – Renderings











Infrastructure Project Milestones





Temporary Ramp







Demolition





East County Library and Public Plaza at Gresham City Hall

- WHAT New 95,000 sq. ft. regional library and public plaza adjacent to Gresham City Hall MAX Station
- WHEN Construction is underway. Project completion is scheduled for Fall 2025
- WHAT Excavation and deep soil foundation work in progress. Permit for (non-foundation) building elements under review. Vertical construction forecast late Spring



Library – Exterior Renderings











Library – Interior Renderings











Library – Renderings











Time Lapse Video





TOD webpage updated









Comments/Questions

tod@trimet.org

(503) 962-2190

Lance Erz | Director, Real Estate and TOD

Guy Benn | Program Manager, TOD



